ITC Fiber Assembly Schedule

ID	Task Name	Duration	Start	Finish
1	**ITC Fiber Assemblies**	**576d**	**Mon 8/3/98**	**Mon 10/30/00**
2	**Design ITC fiber assemblies**	**6w**	**Mon 8/3/98**	**Fri 9/11/98**
3	**Prototype ITC fiber assemblies**	**42d**	**Thu 10/15/98**	**Fri 12/11/98**
10	**Produce ITC fiber assemblies**	**481d**	**Mon 12/14/98**	**Mon 10/30/00**
11	Iterate design and drawings	6w	Mon 12/14/98	Fri 1/22/99
12	Find sources for components	6w	Mon 12/14/98	Fri 1/22/99
13	Purchase components	10w	Mon 3/22/99	Fri 5/28/99
14	Design assembly fixtures	2w	Mon 2/1/99	Fri 2/12/99
15	Make assembly fixtures	4w	Mon 4/19/99	Fri 5/14/99
16	**Production (6R+6L/cycle)**	**352d**	**Mon 5/31/99**	**Mon 10/16/00**
17	**Production cycle 1**	**22d**	**Mon 5/31/99**	**Wed 6/30/99**
49	Production cycle 2	3w	Thu 7/1/99	Thu 7/22/99
50	Production cycle 3	3w	Fri 7/23/99	Thu 8/12/99
51	Production cycle 4	3w	Fri 8/13/99	Thu 9/2/99
52	Production cycle 5	3w	Fri 9/3/99	Fri 9/24/99
53	Production cycle 6	3w	Mon 9/27/99	Fri 10/15/99
54	Production cycle 7	3w	Mon 10/18/99	Fri 11/5/99
55	Production cycle 8	3w	Mon 11/8/99	Tue 11/30/99
56	Production cycle 9	3w	Wed 12/1/99	Tue 12/21/99
57	Production cycle 10	3w	Wed 12/22/99	Mon 1/17/00
58	Production cycle 11	3w	Tue 1/18/00	Mon 2/7/00
59	Production cycle 12	3w	Tue 2/8/00	Mon 2/28/00
60	Production cycle 13	3w	Tue 2/29/00	Mon 3/20/00
61	Production cycle 14	3w	Tue 3/21/00	Mon 4/10/00
62	Production cycle 15	3w	Tue 4/11/00	Mon 5/1/00
63	Production cycle 16	3w	Tue 5/2/00	Mon 5/22/00
64	Production cycle 17	3w	Tue 5/23/00	Mon 6/12/00
65	Production cycle 18	3w	Tue 6/13/00	Mon 7/3/00
66	Production cycle 19	3w	Tue 7/4/00	Mon 7/24/00
67	Production cycle 20	3w	Tue 7/25/00	Mon 8/14/00
68	Production cycle 21	3w	Tue 8/15/00	Mon 9/4/00
69	Production cycle 22	3w	Tue 9/5/00	Mon 9/25/00
70	Production cycle 23	3w	Tue 9/26/00	Mon 10/16/00
71	Shipments to ANL	290d	Fri 9/3/99	Mon 10/23/00
75	Shipments to BCN	325d	Fri 7/23/99	Mon 10/30/00
79	*Start of Production*	*0d*	*Mon 5/31/99*	*Mon 5/31/99*
80	*First delivery to ANL*	*0d*	*Fri 9/10/99*	*Fri 9/10/99*
81	*First delivery to BCN*	*0d*	*Mon 8/9/99*	*Mon 8/9/99*
82	*Final delivery to ANL*	*0d*	*Mon 10/23/00*	*Mon 10/23/00*
83	*Final delivery to BCN*	*0d*	*Mon 10/30/00*	*Mon 10/30/00*

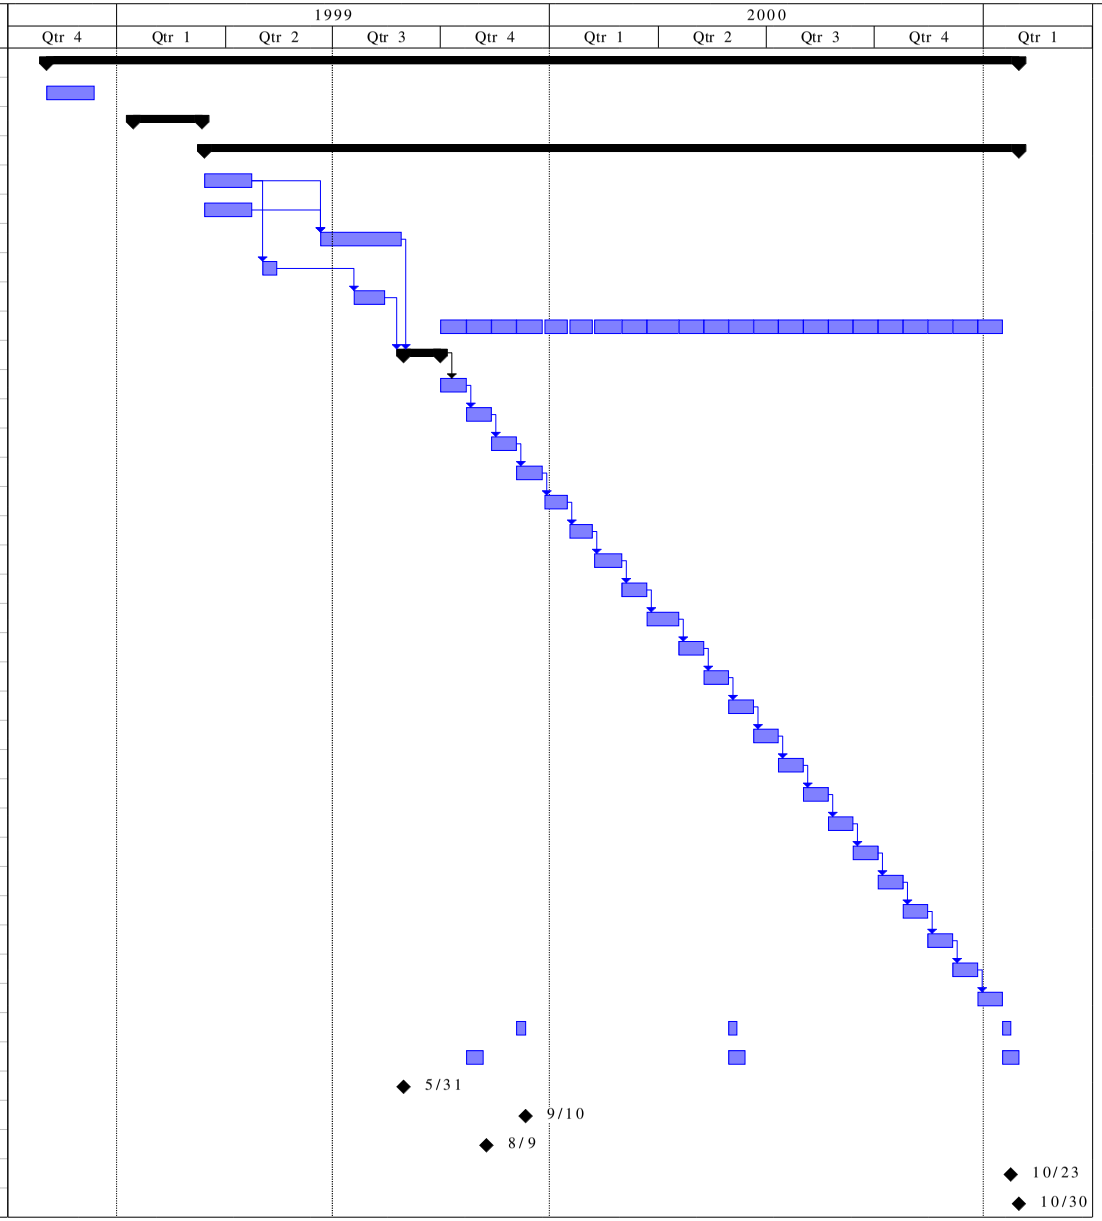

Project: ITC Fiber Assemblies
Date: Thu 4/1/99

Task | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Milestone | Rolled Up Progress
