ID	Task Name	Duration	Start	Finish
1	**ITC Fiber Assemblies**	**519d**	**Mon 8/3/98**	**Fri 7/28/00**
2	**Design ITC fiber assemblies**	**6w**	**Mon 8/3/98**	**Fri 9/11/98**
3	**Prototype ITC fiber assemblies**	**42d**	**Thu 10/15/98**	**Fri 12/11/98**
4	Prepare components for Prototype	4w	Thu 10/15/98	Wed 11/11/98
5	Develop assembly procedure	4w	Mon 10/19/98	Fri 11/13/98
6	Make prototypes (1L+1R)	2w	Mon 11/16/98	Fri 11/27/98
7	Ship prototype to UTA	1w	Mon 11/30/98	Fri 12/4/98
8	Test prototypes	1w	Mon 12/7/98	Fri 12/11/98
9	*Protoypes finished*	*0d*	*Fri 12/11/98*	*Fri 12/11/98*
10	**Produce ITC fiber assemblies**	**424d**	**Mon 12/14/98**	**Fri 7/28/00**
11	Iterate design and drawings	4w	Mon 12/14/98	Fri 1/8/99
12	Find sources for components	4w	Mon 12/14/98	Fri 1/8/99
13	Purchase components	5w	Mon 1/11/99	Fri 2/12/99
14	Design assembly fixtures	2w	Mon 1/11/99	Fri 1/22/99
15	Make assembly fixtures	3w	Mon 1/25/99	Fri 2/12/99
16	Production (6R+6L/cycle)	360d	Mon 2/15/99	Fri 6/30/00
41	*Start of Production*	*0d*	*Mon 2/22/99*	*Mon 2/22/99*
42	Shipments to ANL	305d	Mon 5/10/99	Fri 7/7/00
46	*First delivery to ANL*	*0d*	*Fri 5/28/99*	*Fri 5/28/99*
47	*Final delivery to ANL*	*0d*	*Fri 7/28/00*	*Fri 7/28/00*
48	Shipments to BCN	310d	Mon 5/10/99	Fri 7/14/00
52	*First delivery to BCN*	*0d*	*Fri 6/4/99*	*Fri 6/4/99*
53	*Fnal delivery to BCN*	*0d*	*Fri 7/28/00*	*Fri 7/28/00*

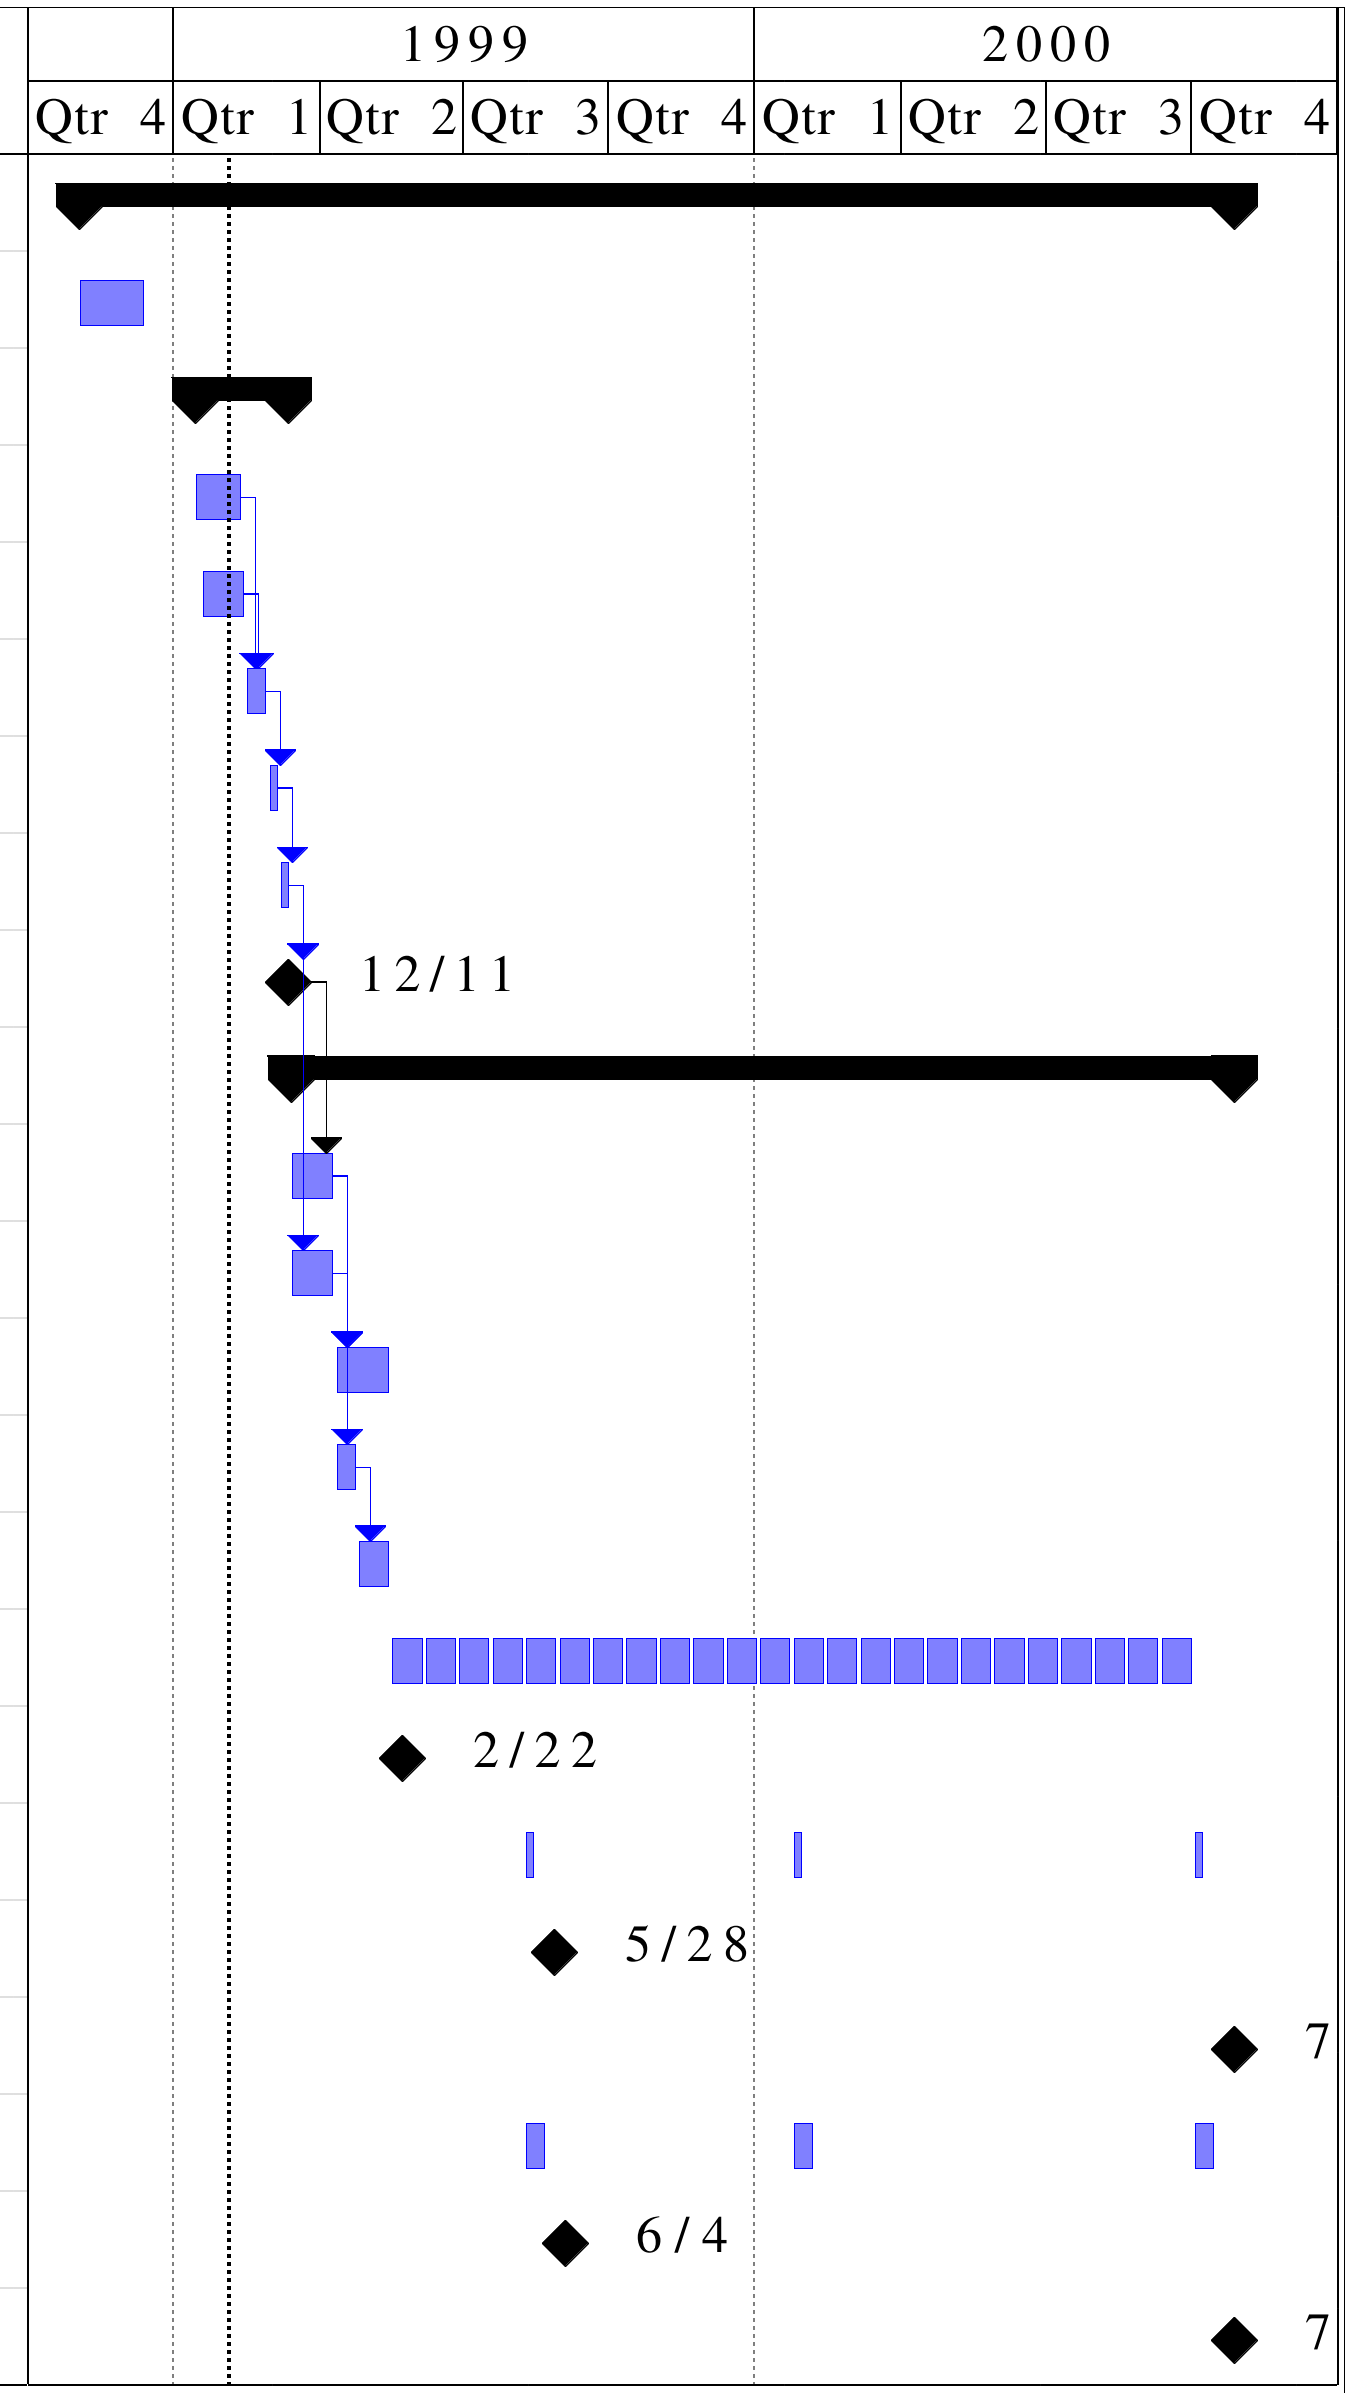

Project: ITC Fiber Assemblies
Date: Thu 11/5/98

Task	Milestone	Rolled Up Task	Rolled Up Progress
Progress	Summary	Rolled Up Milestone	
